


View: Gantt Chart
Clipboard: Paste, Copy, Format Painter
Font: Calibri, 11, Bold, Italic, Underline, Color, Background Color
Schedule: Mark on Track, Respect Links, Inactivate, Progress Indicators (0%, 25%, 50%, 75%, 100%)
Tasks: Manually Schedule, Auto Schedule, Inspect, Move, Mode
Insert: Task, Summary, Milestone, Deliverable
Properties: Information, Notes, Details, Add to Timeline
Link To: Planner
Editing: Find, Clear, Fill

Task Mode	Task Name	Start	Finish	Resource Names	% Complete	Remaining
1		Thu 9/1/22	Mon 12/2/24		58%	245.05
16	2209 Tickets	Mon 3/20/23	Wed 7/17/24		40%	207.47
18	2209 Draw Tickets	Mon 4/17/23	Wed 7/17/24	John, Jane [50%]	31%	124.13
19	2209 Check Tickets	Fri 4/14/23	Fri 4/26/24	Joe [10%]	20%	552 hrs
20	2209 Sample Approved	Thu 9/1/22	Thu 9/1/22		0%	0 days
25	2209 Production	Wed 3/20/24	Thu 7/11/24	Production[846 Piece]	0%	82 days
26	2209	Tue 8/13/24	Mon 12/2/24	Erection[846 Piece]	0%	80 days
3	2301	Mon 3/6/23	Mon 4/1/24		67%	93.12
4	2302	Fri 7/14/23	Thu 10/10/24		57%	138.58
5	2303	Fri 5/5/23	Tue 4/9/24		92%	18.32
6	2304	Mon 3/13/23	Fri 6/7/24		43%	186.24
7	2305	Fri 7/28/23	Tue 4/23/24		62%	72.96
8	2306	Mon 10/9/23	Mon 8/5/24		30%	150.66
9	2307	Mon 11/6/23	Fri 11/22/24		20%	218.75
10	2308	Mon 11/6/23	Tue 3/11/25		11%	311.61
11	2309	Mon 11/6/23	Tue 7/1/25		14%	371.52
12	2310	Mon 11/6/23	Fri 10/17/25		13%	444.96

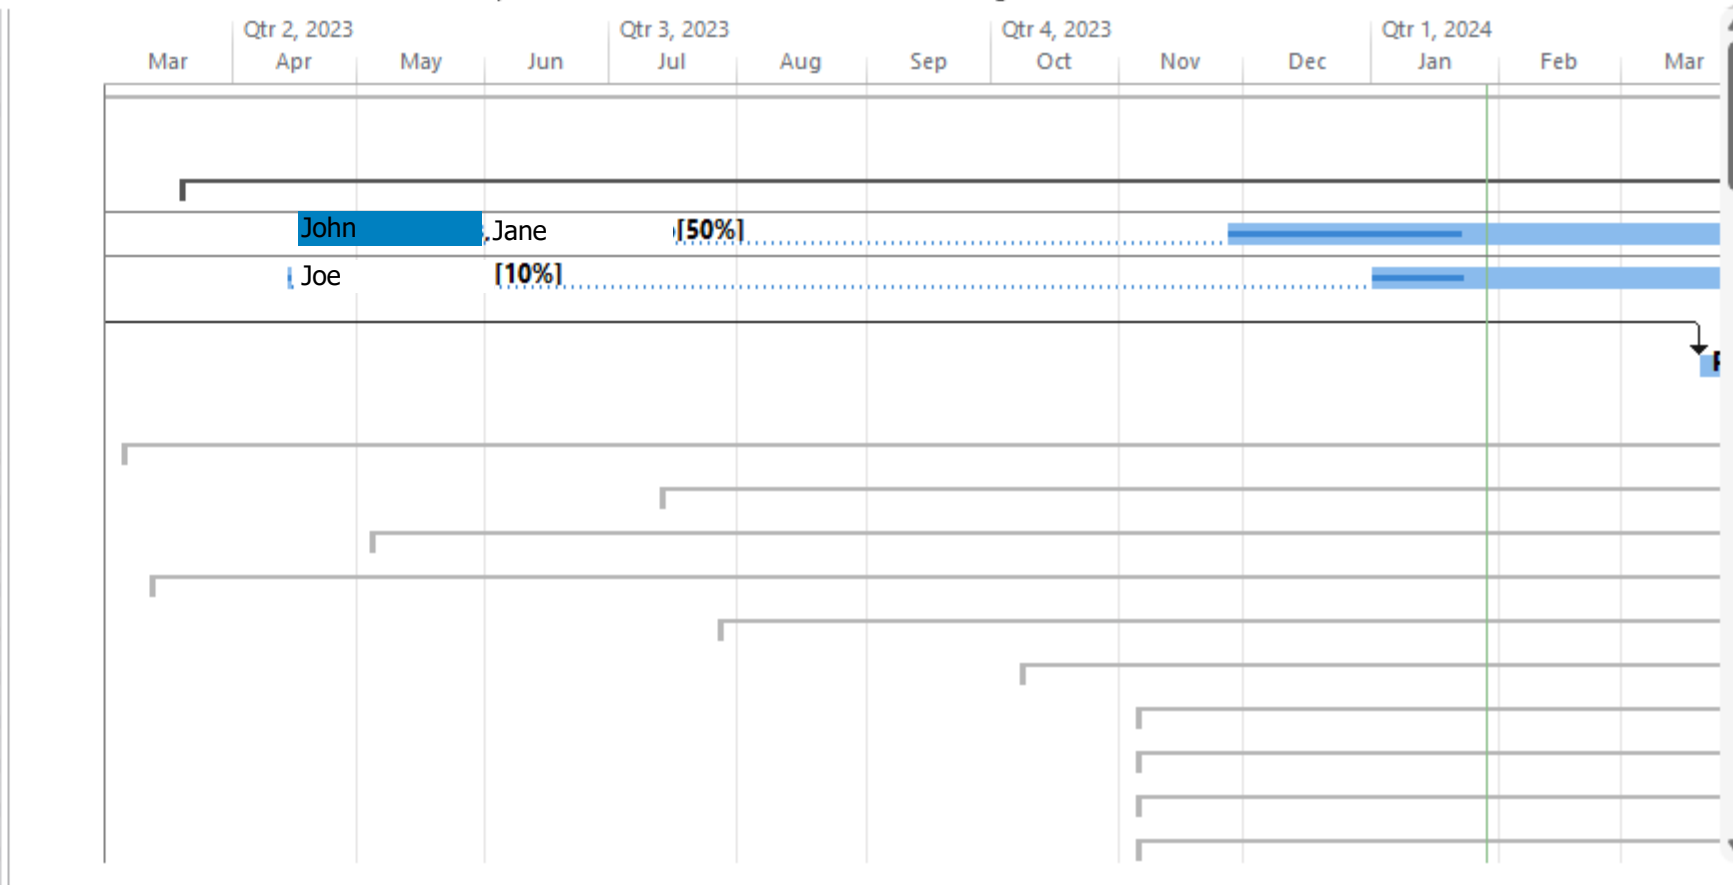

Task Mode	Task Name	Work	Remaining Work	Duration	Start	Finish	Resource Name
18	2209 Draw Tickets	731.34 hrs	496.5 hrs	179.13 days	Mon 4/17/23	Wed 7/17/24	
	John	57 hrs	0 hrs		Mon 4/17/23	Fri 5/5/23	
	Jane	574.34 hrs	496.5 hrs		Mon 4/17/23	Wed 7/17/24	

Details	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
Work		39h	18h	0h	0h	0h	0h	0h	10.4h	54.74h	140.7h	84h	8h
Work		39h	18h	0h									
Work		0h	0h	0h	0h	0h	0h	0h	10.4h	54.74h	140.7h	84h	8h
